


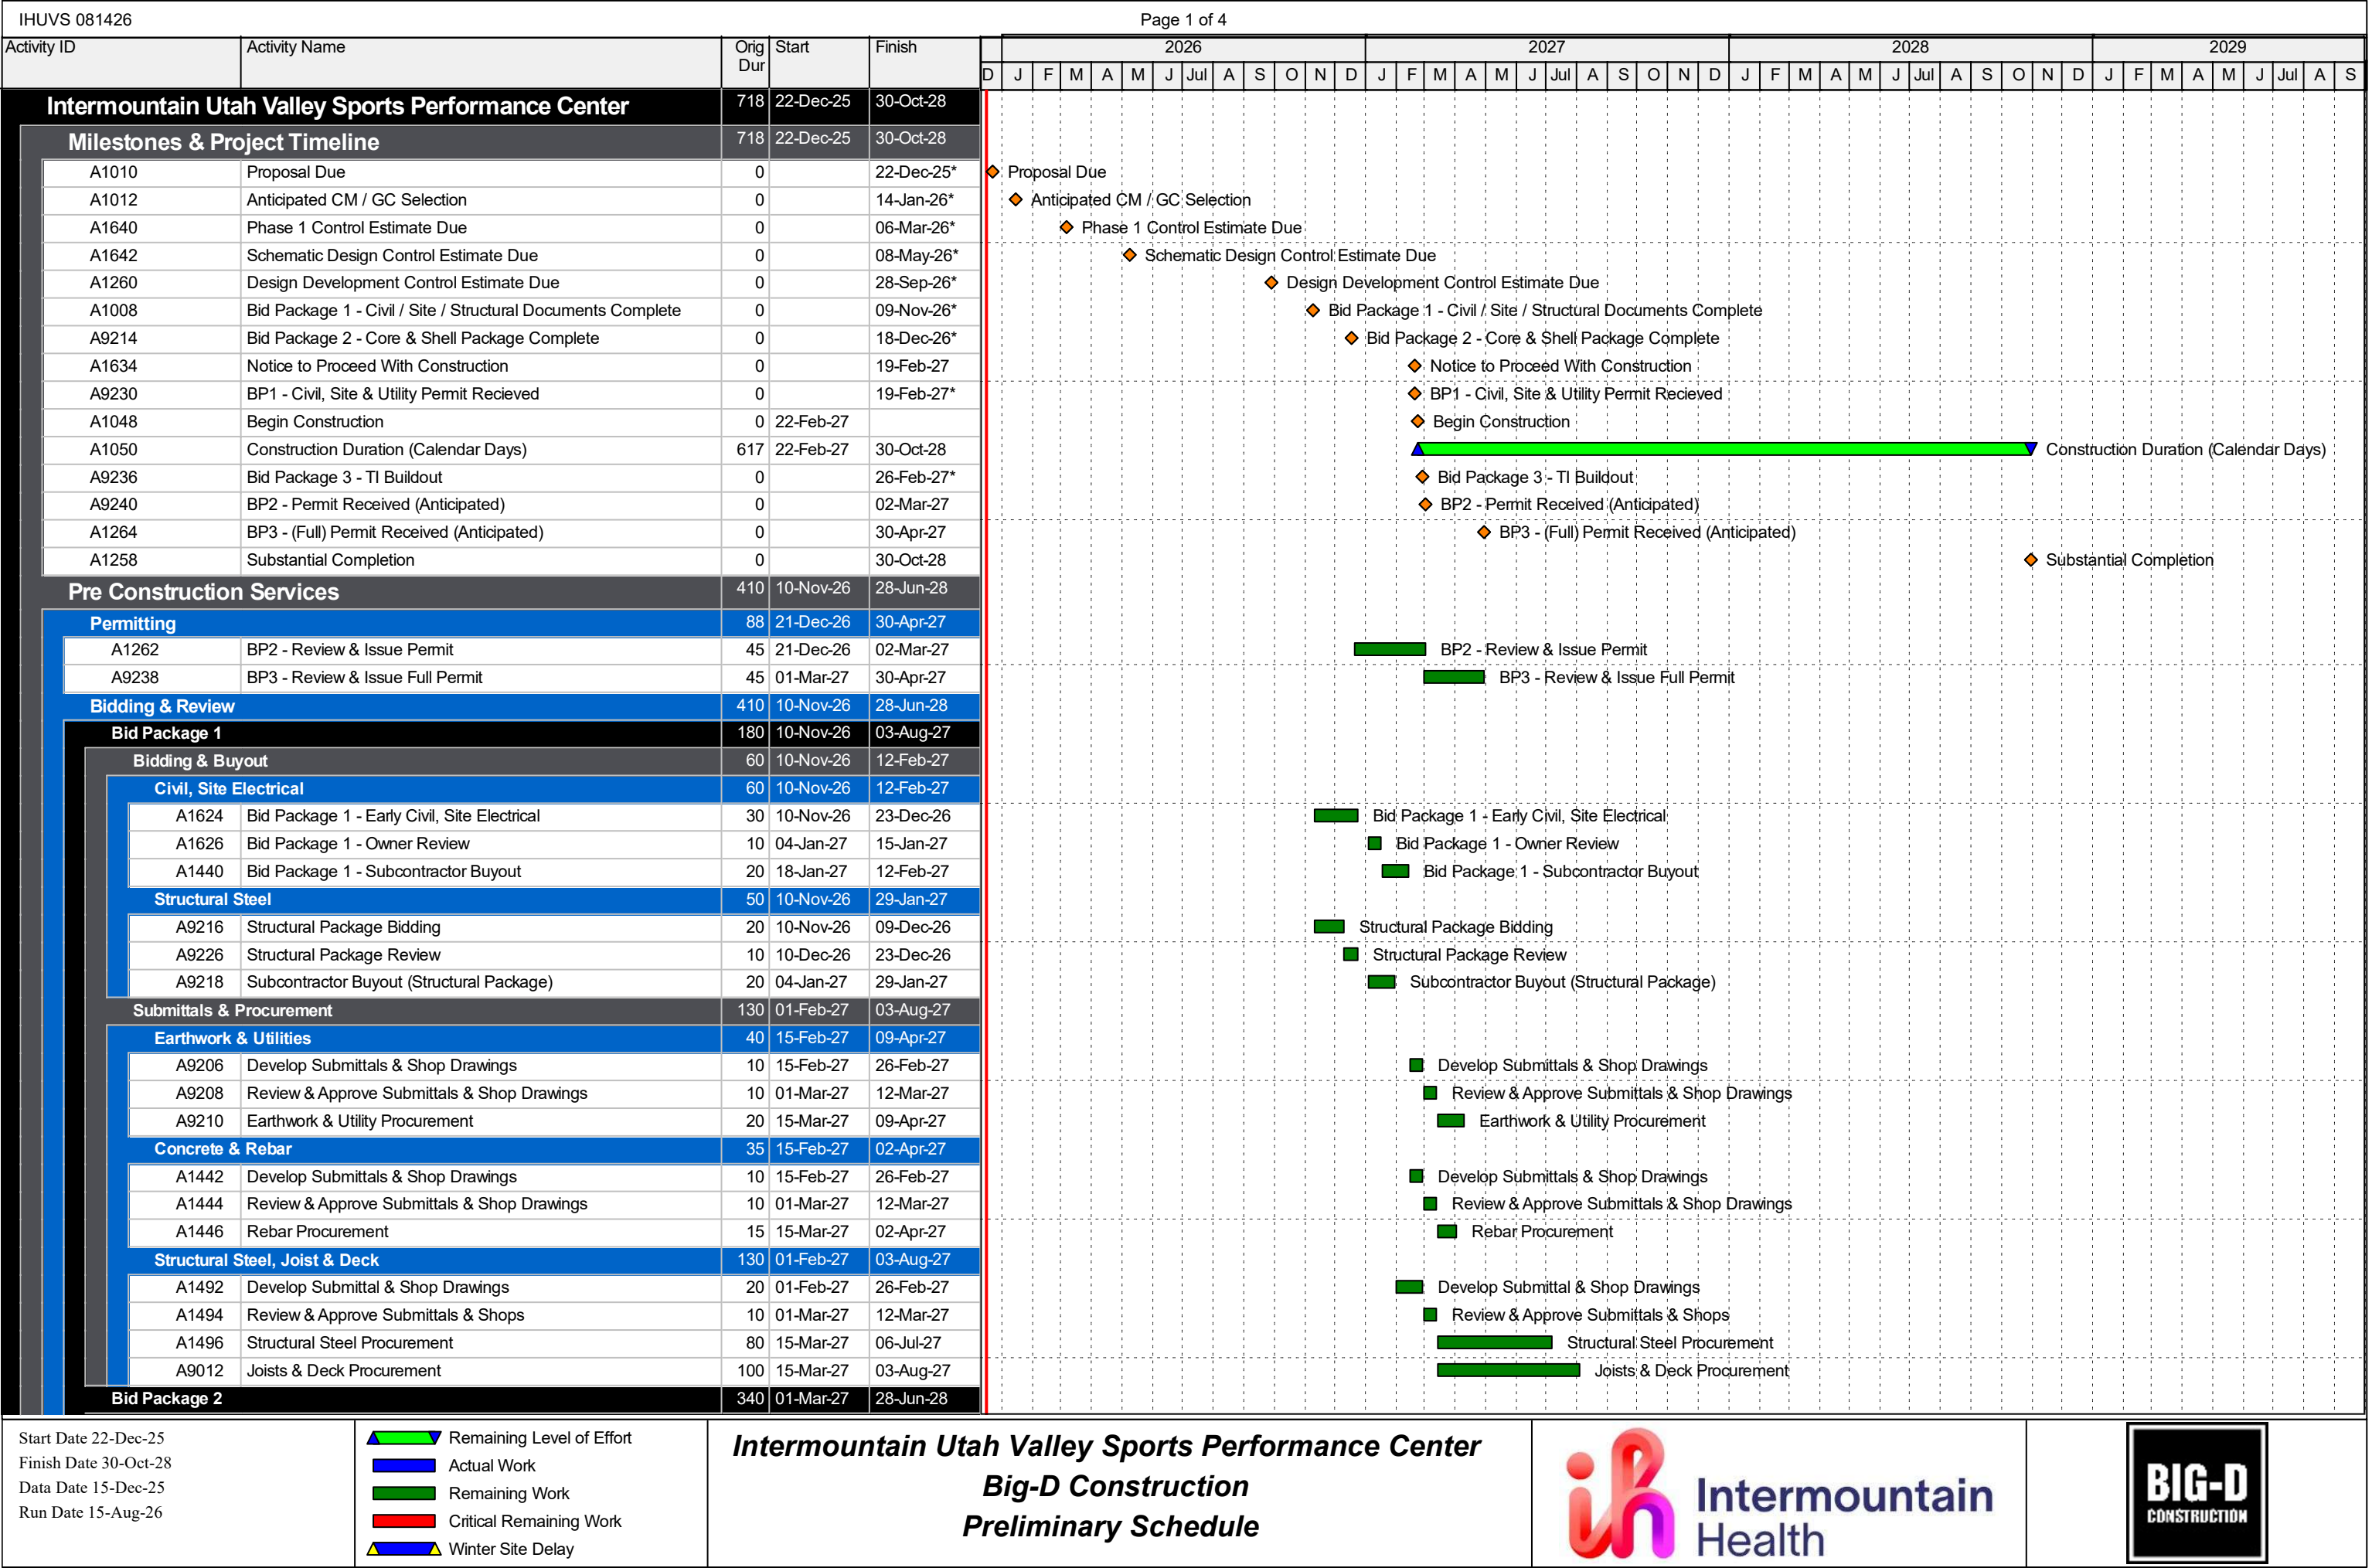

| Activity ID |                                                | Activity Name                                              | Orig Dur  | Start     | Finish                                                 | 2026                                                                                  |   |   |   |   |   |   |     |   |   |   |   | 2027 |   |   |   |   |   |   |     |   |   |   |   | 2028 |   |   |   |   |   |   |     |   |   |   |   | 2029 |   |   |   |   |   |   |     |   |   |  |  |
|-------------|------------------------------------------------|------------------------------------------------------------|-----------|-----------|--------------------------------------------------------|---------------------------------------------------------------------------------------|---|---|---|---|---|---|-----|---|---|---|---|------|---|---|---|---|---|---|-----|---|---|---|---|------|---|---|---|---|---|---|-----|---|---|---|---|------|---|---|---|---|---|---|-----|---|---|--|--|
|             |                                                |                                                            |           |           |                                                        | D                                                                                     | J | F | M | A | M | J | Jul | A | S | O | N | D    | J | F | M | A | M | J | Jul | A | S | O | N | D    | J | F | M | A | M | J | Jul | A | S | O | N | D    | J | F | M | A | M | J | Jul | A | S |  |  |
| Activity ID | Bidding & Buyout                               |                                                            | 50        | 01-Mar-27 | 07-May-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A9222                                          | Bid Package 2 - Subcontractor Bidding (Bldg. Core & Shell) | 20        | 01-Mar-27 | 26-Mar-27                                              | <div><div></div> Bid Package 2 - Subcontractor Bidding (Bldg. Core &amp; Shell)</div> |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A9224                                          | Bid Package 2 - Owner Review (Bldg. Core & Shell)          | 10        | 29-Mar-27 | 09-Apr-27                                              | <div><div></div> Bid Package 2 - Owner Review (Bldg. Core &amp; Shell)</div>          |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A9212                                          | Bid Package 2 - Subcontractor Buyout (Bldg. Core & Shell)  | 20        | 12-Apr-27 | 07-May-27                                              | <div><div></div> Bid Package 2 - Subcontractor Buyout (Bldg. Core &amp; Shell)</div>  |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Procurement, Submittals & Fabrication          |                                                            | 290       | 10-May-27 | 28-Jun-28                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Roofing System                                 |                                                            | 80        | 10-May-27 | 31-Aug-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1484                                          | Develop Submittals & Shop Drawings                         | 10        | 10-May-27 | 21-May-27                                              | <div><div></div> Develop Submittals &amp; Shop Drawings</div>                         |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1486                                          | Review & Approve Submittals & Shop Drawings                | 10        | 24-May-27 | 07-Jun-27                                              | <div><div></div> Review &amp; Approve Submittals &amp; Shop Drawings</div>            |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1488                                          | Roofing System Procurement                                 | 60        | 08-Jun-27 | 31-Aug-27                                              | <div><div></div> Roofing System Procurement</div>                                     |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Exterior Skin System, Windows & Doors          |                                                            | 100       | 10-May-27 | 29-Sep-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1462                                          | Develop Submittals & Shop Drawings                         | 10        | 10-May-27 | 21-May-27                                              | <div><div></div> Develop Submittals &amp; Shop Drawings</div>                         |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1464                                          | Review & Approve Submittals & Shop Drawings                | 10        | 24-May-27 | 07-Jun-27                                              | <div><div></div> Review &amp; Approve Submittals &amp; Shop Drawings</div>            |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1466                                          | Exterior Skin Procurement                                  | 80        | 08-Jun-27 | 29-Sep-27                                              | <div><div></div> Exterior Skin Procurement</div>                                      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Framing & Drywall                              |                                                            | 20        | 10-May-27 | 07-Jun-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1468                                          | Develop Submittals & Shop Drawings                         | 10        | 10-May-27 | 21-May-27                                              | <div><div></div> Develop Submittals &amp; Shop Drawings</div>                         |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1470                                          | Review & Approve Submittals & Shop Drawings                | 10        | 24-May-27 | 07-Jun-27                                              | <div><div></div> Review &amp; Approve Submittals &amp; Shop Drawings</div>            |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Elevators                                      |                                                            | 110       | 10-May-27 | 13-Oct-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A9018                                          | Develop Submittals & Shop Drawings                         | 20        | 10-May-27 | 07-Jun-27                                              | <div><div></div> Develop Submittals &amp; Shop Drawings</div>                         |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A9020                                          | Review & Approve Submittals & Shop Drawings                | 10        | 08-Jun-27 | 21-Jun-27                                              | <div><div></div> Review &amp; Approve Submittals &amp; Shop Drawings</div>            |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A9022                                          | Elevator Procurement                                       | 80        | 22-Jun-27 | 13-Oct-27                                              | <div><div></div> Elevator Procurement</div>                                           |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | MEPS (Mechanical, Elec., Plumbing & Sprinkler) |                                                            | 290       | 10-May-27 | 28-Jun-28                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1454                                          | Develop Submittals & Shop Drawings                         | 20        | 10-May-27 | 07-Jun-27                                              | <div><div></div> Develop Submittals &amp; Shop Drawings</div>                         |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1456                                          | Review & Approve Submittals & Shop Drawings                | 10        | 08-Jun-27 | 21-Jun-27                                              | <div><div></div> Review &amp; Approve Submittals &amp; Shop Drawings</div>            |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1458                                          | Long Lead Mechanical Procurement                           | 120       | 22-Jun-27 | 10-Dec-27                                              | <div><div></div> Long Lead Mechanical Procurement</div>                               |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1460                                          | Mechanical Duct Procurement                                | 50        | 22-Jun-27 | 31-Aug-27                                              | <div><div></div> Mechanical Duct Procurement</div>                                    |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1632                                          | Back-Up Generator Procurement                              | 260       | 22-Jun-27 | 28-Jun-28                                              | <div><div></div> Back-Up Generator Procurement</div>                                  |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1706                                          | Electrical Gear Procurement                                | 220       | 22-Jun-27 | 02-May-28                                              | <div><div></div> Electrical Gear Procurement</div>                                    |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A9232                                          | AHU Early Procurement                                      | 80        | 22-Jun-27 | 13-Oct-27                                              | <div><div></div> AHU Early Procurement</div>                                          |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Building Finishes                              |                                                            | 90        | 10-May-27 | 15-Sep-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1472                                          | Develop Submittals & Shop Drawings                         | 30        | 10-May-27 | 21-Jun-27                                              | <div><div></div> Develop Submittals &amp; Shop Drawings</div>                         |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1474                                          | Review & Approve Submittals & Shop Drawings                | 10        | 22-Jun-27 | 06-Jul-27                                              | <div><div></div> Review &amp; Approve Submittals &amp; Shop Drawings</div>            |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1476                                          | Building Finishes Procurement                              | 50        | 07-Jul-27 | 15-Sep-27                                              | <div><div></div> Building Finishes Procurement</div>                                  |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Site Work & Landscaping                        |                                                            | 60        | 10-May-27 | 03-Aug-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1478                                          | Develop Submittals & Shop Drawings                         | 10        | 10-May-27 | 21-May-27                                              | <div><div></div> Develop Submittals &amp; Shop Drawings</div>                         |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1480                                          | Review & Approve Submittals & Shop Drawings                | 10        | 24-May-27 | 07-Jun-27                                              | <div><div></div> Review &amp; Approve Submittals &amp; Shop Drawings</div>            |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1482                                          | Landscaping Procurement                                    | 40        | 08-Jun-27 | 03-Aug-27                                              | <div><div></div> Landscaping Procurement</div>                                        |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Construction Services                          |                                                            | 376       | 22-Feb-27 | 11-Aug-28                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | Earthwork & Stucture                           |                                                            | 160       | 22-Feb-27 | 06-Oct-27                                              |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1266                                          | Mobilization                                               | 5         | 22-Feb-27 | 26-Feb-27                                              | <div><div></div> Mobilization</div>                                                   |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1382                                          | SWPPP & Site Fencing                                       | 5         | 22-Feb-27 | 26-Feb-27                                              | <div><div></div> SWPPP &amp; Site Fencing</div>                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1646                                          | Site Demo                                                  | 10        | 01-Mar-27 | 12-Mar-27                                              | <div><div></div> Site Demo</div>                                                      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1644                                          | Clear & Grub                                               | 4         | 05-Mar-27 | 10-Mar-27                                              | <div><div></div> Clear &amp; Grub</div>                                               |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1316                                          | Excavate Footings                                          | 15        | 11-Mar-27 | 31-Mar-27                                              | <div><div></div> Excavate Footings</div>                                              |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1318                                          | Place UG Utility Sleeves                                   | 10        | 01-Apr-27 | 14-Apr-27                                              | <div><div></div> Place UG Utility Sleeves</div>                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1344                                          | Early Site Utilities                                       | 20        | 12-Apr-27 | 07-May-27                                              | <div><div></div> Early Site Utilities</div>                                           |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1320                                          | Form & Place Footings                                      | 22        | 15-Apr-27 | 14-May-27                                              | <div><div></div> Form &amp; Place Footings</div>                                      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1322                                          | Form & Place Foundations Walls                             | 25        | 29-Apr-27 | 03-Jun-27                                              | <div><div></div> Form &amp; Place Foundations Walls</div>                             |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1324                                          | Install Foundation Insulation & Backfill                   | 10        | 27-May-27 | 10-Jun-27                                              | <div><div></div> Install Foundation Insulation &amp; Backfill</div>                   |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1326                                          | Install UG Utilities                                       | 20        | 04-Jun-27 | 01-Jul-27                                              | <div><div></div> Install UG Utilities</div>                                           |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
|             | A1328                                          | Prep & Place SOG                                           | 20        | 18-Jun-27 | 16-Jul-27                                              | <div><div></div> Prep &amp; Place SOG</div>                                           |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
| A1374       | Erect Steel, Beams & Joists                    | 30                                                         | 19-Jul-27 | 27-Aug-27 | <div><div></div> Erect Steel, Beams &amp; Joists</div> |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
| A1428       | Metal Decking                                  | 15                                                         | 16-Aug-27 | 03-Sep-27 | <div><div></div> Metal Decking</div>                   |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |
| A1430       | In-Slab MEP & Sleeves                          | 12                                                         | 07-Sep-27 | 22-Sep-27 | <div><div></div> In-Slab MEP &amp; Sleeves</div>       |                                                                                       |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |   |   |      |   |   |   |   |   |   |     |   |   |  |  |

[illegible]

[illegible]
